






















Id	Task Name	Duración	Comienzo	Fin	01 abr '13							08 abr '13							15 abr '13						
					S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V
1	LICEO COPEYITO	144 días?	sáb 30/03/13	sáb 14/09/13																					
2	Preliminares	5 días	sáb 30/03/13	vie 05/04/13																					
3	Letrero en Obra	1 día	sáb 30/03/13	lun 01/04/13																					
4	Caseta de Materiales	2 días	lun 01/04/13	mié 03/04/13																					
5	Acondicionamiento de Terreno	4 días	lun 01/04/13	vie 05/04/13																					
6	BLOQUE B1	144 días?	sáb 30/03/13	sáb 14/09/13																					
7	B-1 >> 1er. NIVEL	116 días?	sáb 30/03/13	mar 13/08/13																					
8	Replanteo	2 días	vie 05/04/13	lun 08/04/13																					
9	Movimientos de Tierra	23 días	lun 08/04/13	sáb 04/05/13																					
12	Muros de Bloques	24 días	sáb 20/04/13	sáb 18/05/13																					
15	Hormigones	41 días	mié 17/04/13	mar 04/06/13																					
21	Terminacion de Superficies	21 días	mar 04/06/13	vie 28/06/13																					
22	Terminacion de Escalera	1 día?	vie 28/06/13	sáb 29/06/13																					
23	Terminacion de Piso	10 días	sáb 29/06/13	jue 11/07/13																					
24	Portaje Ventana y Protectores	10 días	jue 11/07/13	mar 23/07/13																					
25	Revestimiento de baño	1 día?	mar 23/07/13	mié 24/07/13																					
26	Plafones	1 día?	mié 24/07/13	jue 25/07/13																					
27	Aceras perimetrales	1 día?	jue 25/07/13	vie 26/07/13																					
28	Pintura	15 días	vie 26/07/13	mar 13/08/13																					
29	Varios	1 día?	sáb 30/03/13	lun 01/04/13																					
30	B-1>> 2do. NIVEL	144 días?	sáb 30/03/13	sáb 14/09/13																					
31	Replanteo	2 días	mar 04/06/13	jue 06/06/13																					
32	Muros de Bloques	10 días	jue 06/06/13	mar 18/06/13																					
33	Hormigones	19 días	mar 18/06/13	mié 10/07/13																					
36	Terminacion de Superficies	25 días	mié 10/07/13	jue 08/08/13																					
37	Terminacion de Piso	17 días	jue 08/08/13	mié 28/08/13																					
38	Terminacion de Escalera	7 días	sáb 30/03/13	lun 08/04/13																					
39	Terminacion de techo	1 día?	sáb 30/03/13	lun 01/04/13																					
40	Portaje y Ventanas	10 días	mié 28/08/13	lun 09/09/13																					
41	Barandas	1 día?	sáb 30/03/13	lun 01/04/13																					
42	Revestimiento de baño	1 día?	sáb 30/03/13	lun 01/04/13																					
43	Plafones	1 día?	sáb 30/03/13	lun 01/04/13																					
44	Pintura	15 días	mié 28/08/13	sáb 14/09/13																					

Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

Id	Task Name	Duración	Comienzo	Fin	01 abr '13							08 abr '13							15 abr '13						
					S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V
45	Varios	12 días	mié 10/07/13	mié 24/07/13																					
46	B-1>> 3er. NIVEL (Caja de escalera)	1 día?	sáb 30/03/13	lun 01/04/13																					
47	Replanteo	1 día?	sáb 30/03/13	lun 01/04/13																					
48	Muros de Bloques	1 día?	sáb 30/03/13	lun 01/04/13																					
49	Hormigones	1 día?	sáb 30/03/13	lun 01/04/13																					
54	Terminacion de Superficies	1 día?	sáb 30/03/13	lun 01/04/13																					
55	Terminacion de techo	1 día?	sáb 30/03/13	lun 01/04/13																					
56	Portaje y ventanas	1 día?	sáb 30/03/13	lun 01/04/13																					
57	Pintura	1 día?	sáb 30/03/13	lun 01/04/13																					
58	Varios	1 día?	sáb 30/03/13	lun 01/04/13																					
59	BLOQUE B2 (2 AULAS + DEPOSITO + BAÑO)	150 días?	sáb 30/03/13	sáb 21/09/13																					
60	B-2-1ER NIVEL	1 día?	sáb 30/03/13	lun 01/04/13																					
61	Replanteo	1 día?	sáb 30/03/13	lun 01/04/13																					
62	Muros de Bloques	1 día?	sáb 30/03/13	lun 01/04/13																					
63	Hormigones	1 día?	sáb 30/03/13	lun 01/04/13																					
66	Terminacion de Superficies	1 día?	sáb 30/03/13	lun 01/04/13																					
67	Terminacion de techo	1 día?	sáb 30/03/13	lun 01/04/13																					
68	Terminacion de Piso	1 día?	sáb 30/03/13	lun 01/04/13																					
69	Terminacion de Escalera	1 día?	sáb 30/03/13	lun 01/04/13																					
70	Aceras perimetrales	1 día?	sáb 30/03/13	lun 01/04/13																					
71	Portaje y Ventanas	1 día?	sáb 30/03/13	lun 01/04/13																					
72	Revestimiento de baño	1 día?	sáb 30/03/13	lun 01/04/13																					
73	Protectores metalicos	1 día?	sáb 30/03/13	lun 01/04/13																					
74	Plafones	1 día?	sáb 30/03/13	lun 01/04/13																					
75	Pintura	1 día?	sáb 30/03/13	lun 01/04/13																					
76	Varios	150 días?	sáb 30/03/13	sáb 21/09/13																					
77	COMEDOR 75 PERSONAS	76 días?	sáb 30/03/13	jue 27/06/13																					
78	Replanteo	0.8 días	sáb 30/03/13	sáb 30/03/13																					
79	Muros de Bloques	16 días	sáb 30/03/13	jue 18/04/13																					
80	Hormigones	1 día?	sáb 30/03/13	lun 01/04/13																					
81	Terminacion de Superficies	18.4 días	jue 18/04/13	jue 09/05/13																					
86	Terminacion de Piso	8 días	jue 09/05/13	sáb 18/05/13																					
87	Terminacion de techo	9.6 días	sáb 18/05/13	jue 30/05/13																					


Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

Id	Task Name	Duración	Comienzo	Fin	01 abr '13							08 abr '13							15 abr '13						
					S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V
88	Revestimiento de baño	4 días	jue 09/05/13	mar 14/05/13																					
89	Portaje y Ventanas	8 días	jue 30/05/13	sáb 08/06/13																					
90	Protectores metalicos	8 días	sáb 08/06/13	mar 18/06/13																					
91	Pintura	8 días	sáb 08/06/13	mar 18/06/13																					
92	Aceras perimetrales	2.4 días	sáb 18/05/13	mar 21/05/13																					
93	Pintura	8 días	mar 18/06/13	jue 27/06/13																					
94	Varios	16 días	sáb 27/04/13	jue 16/05/13																					
95	OBRAS COMPLEMENTARIAS	20 días	sáb 30/03/13	mar 23/04/13																					
96	CISTERNA	20 días	sáb 30/03/13	mar 23/04/13																					
97	CAMARA SEPTICA DE DOS CAMARAS	12 días	sáb 30/03/13	sáb 13/04/13																					
98	MISCELANEOS	5.6 días	sáb 30/03/13	vie 05/04/13																					
99	CANCHA MIXTA	22.4 días	sáb 30/03/13	jue 25/04/13																					
100	GRADERIA EN CANCHA	16 días	sáb 30/03/13	jue 18/04/13																					
101	Áreas Exteriores	90 días	sáb 30/03/13	sáb 13/07/13																					
102	Acondicionamiento del Area Exterior	38 días	sáb 30/03/13	mar 14/05/13																					
103	Verja Perimetral	60 días	sáb 04/05/13	sáb 13/07/13																					
104	Caseta de bomba y Cisterna	30 días	sáb 04/05/13	sáb 08/06/13																					
105	Instalaciones Eléctricas y Sanitarias	120 días	sáb 04/05/13	sáb 21/09/13																					
106	Instalacion Electrica General	120 días	sáb 04/05/13	sáb 21/09/13																					
107	Instalacion Sanitaria General	120 días	sáb 04/05/13	sáb 21/09/13																					
108	Adicionales	1 día?	sáb 30/03/13	lun 01/04/13																					
109	LIMPIEZA CONTINUA Y FINAL	1 día?	sáb 30/03/13	lun 01/04/13																					


Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

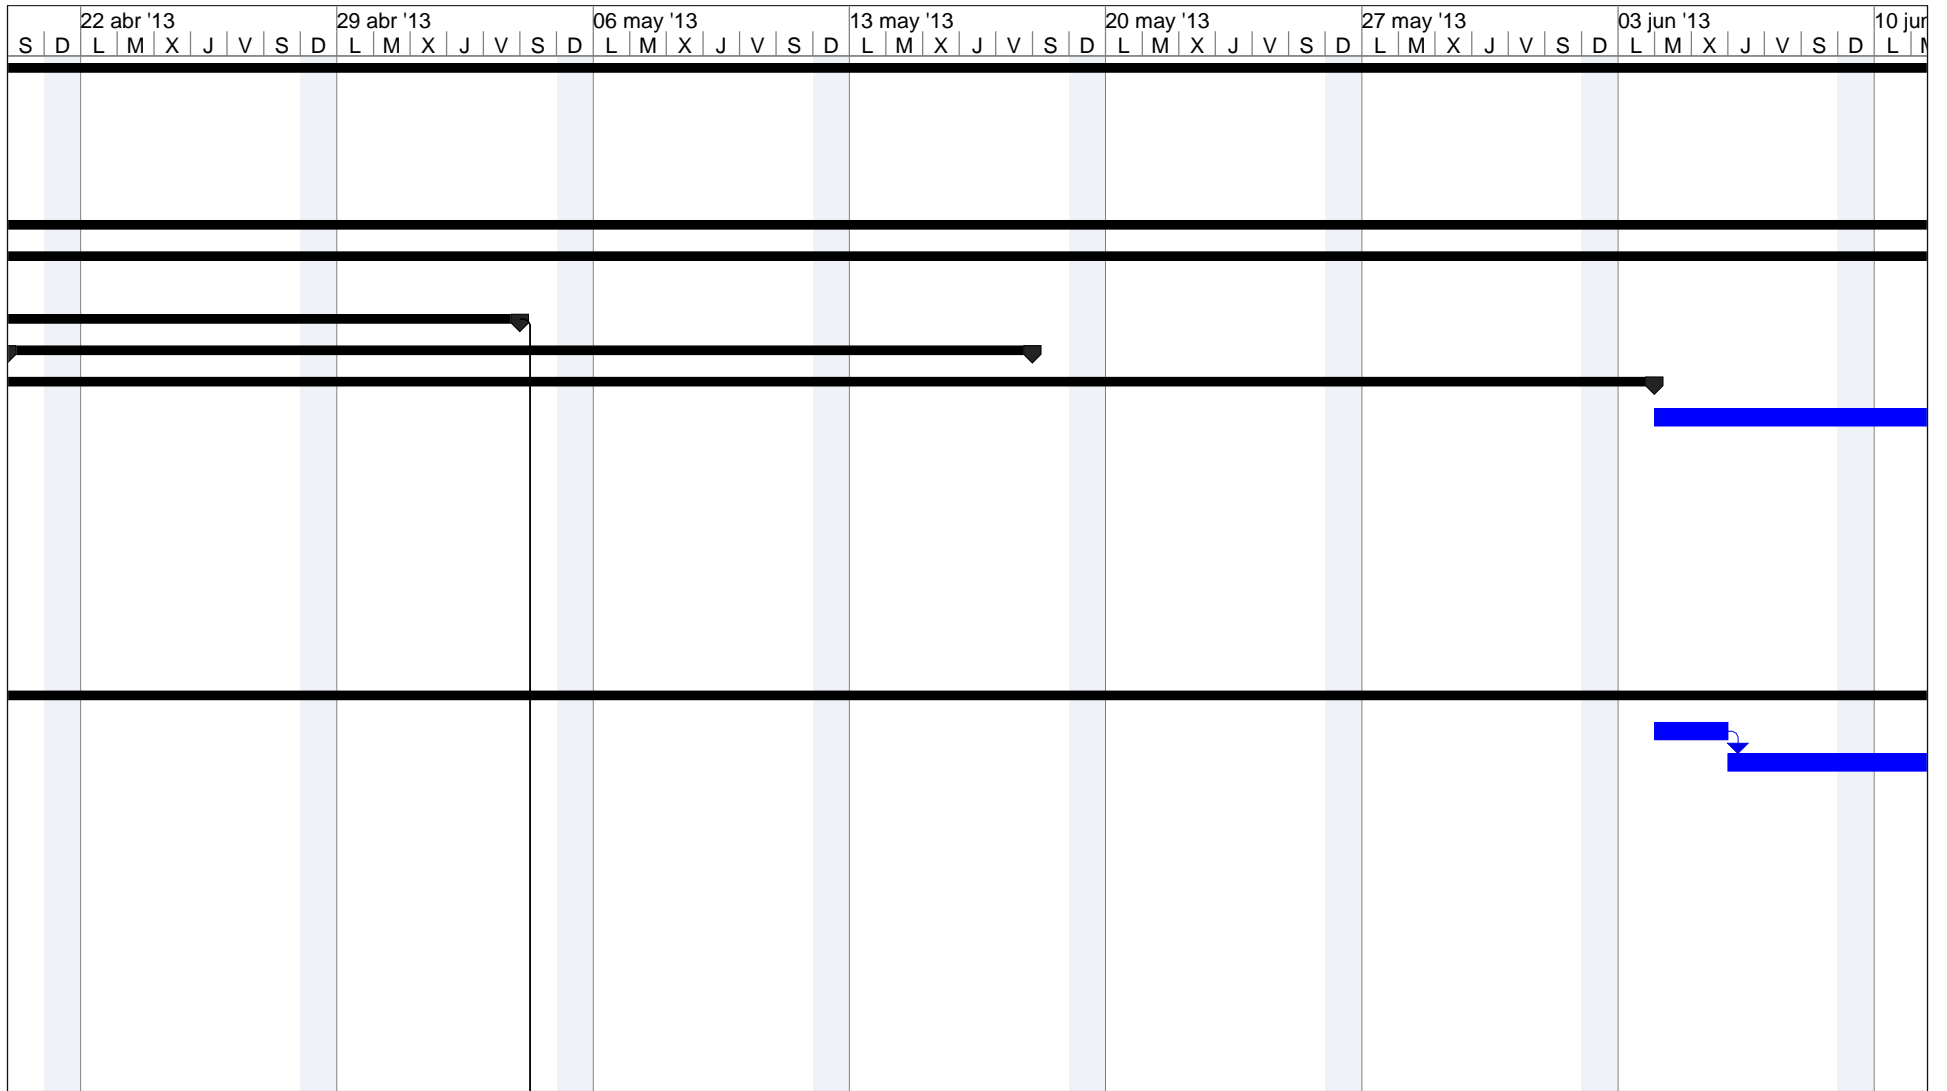


Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

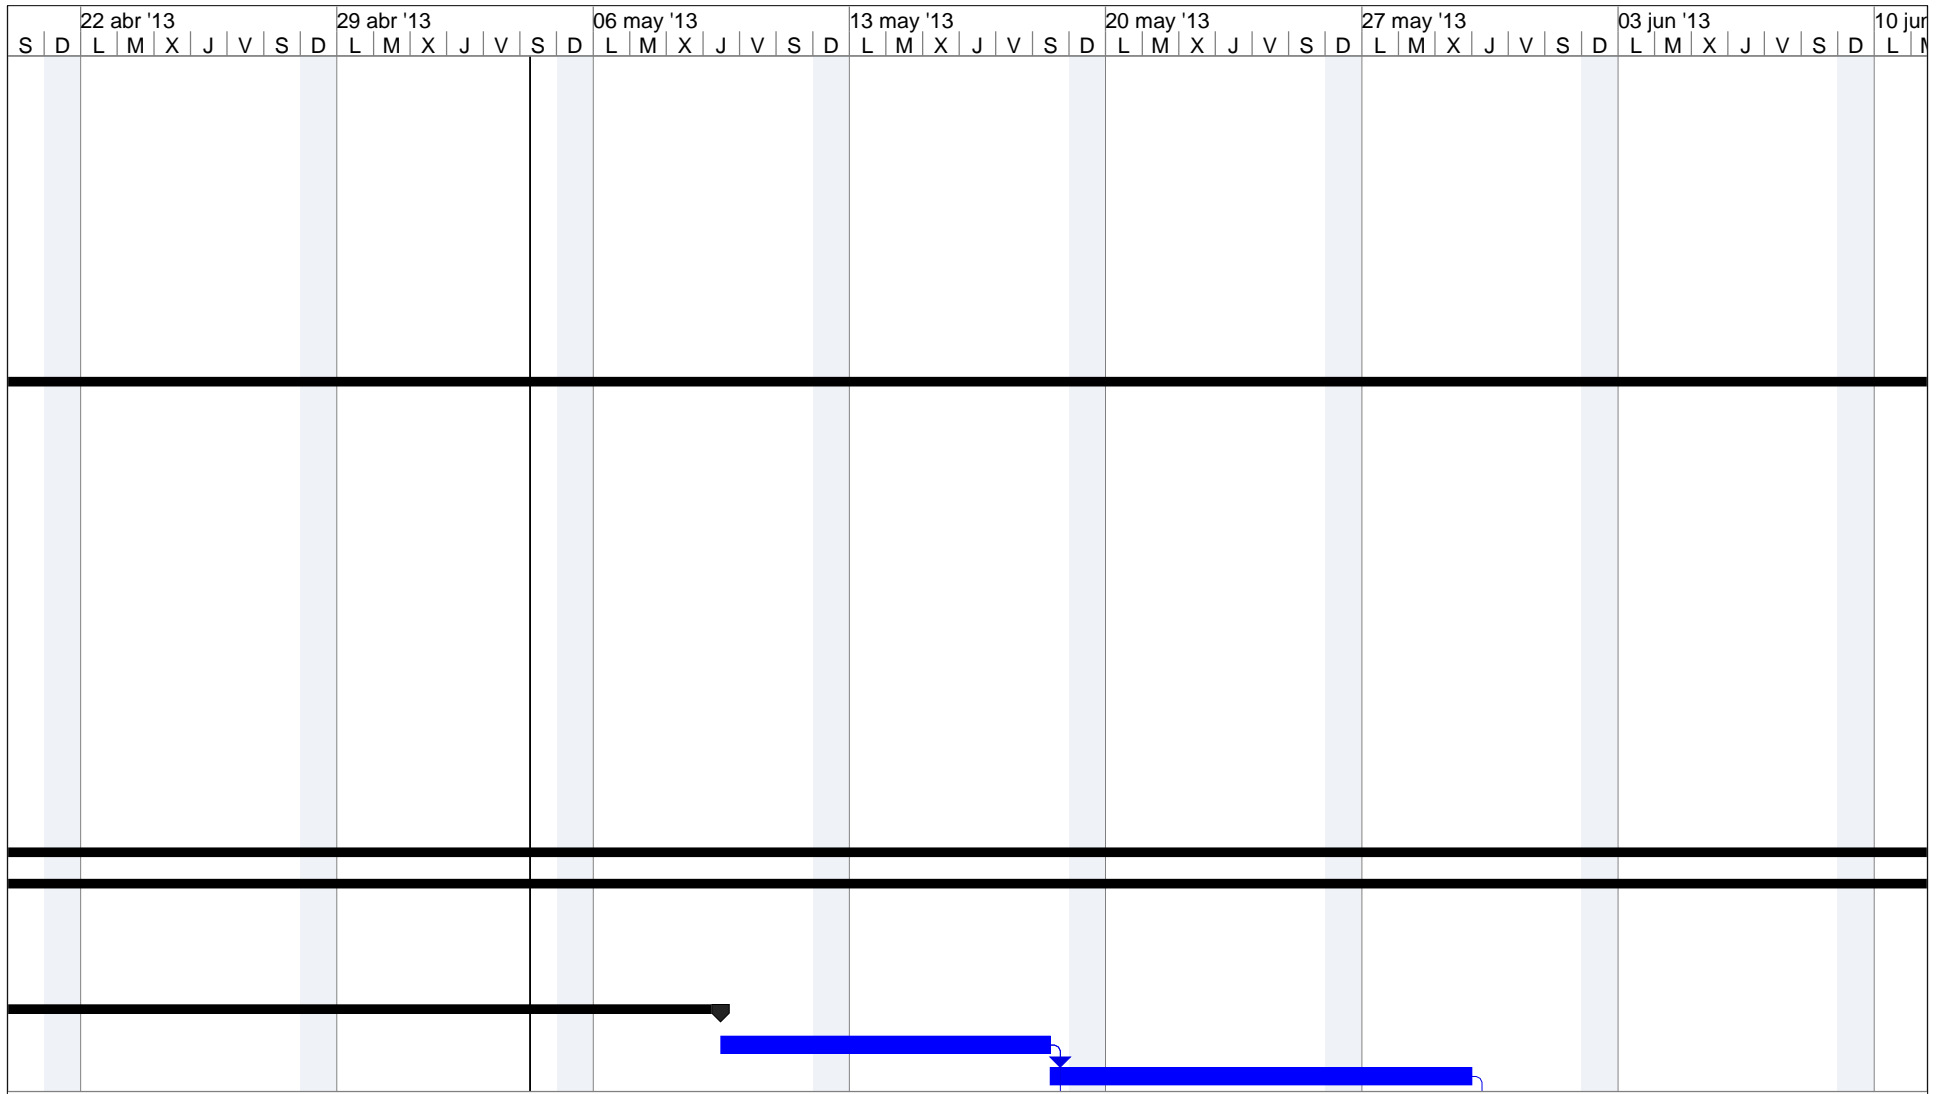


Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

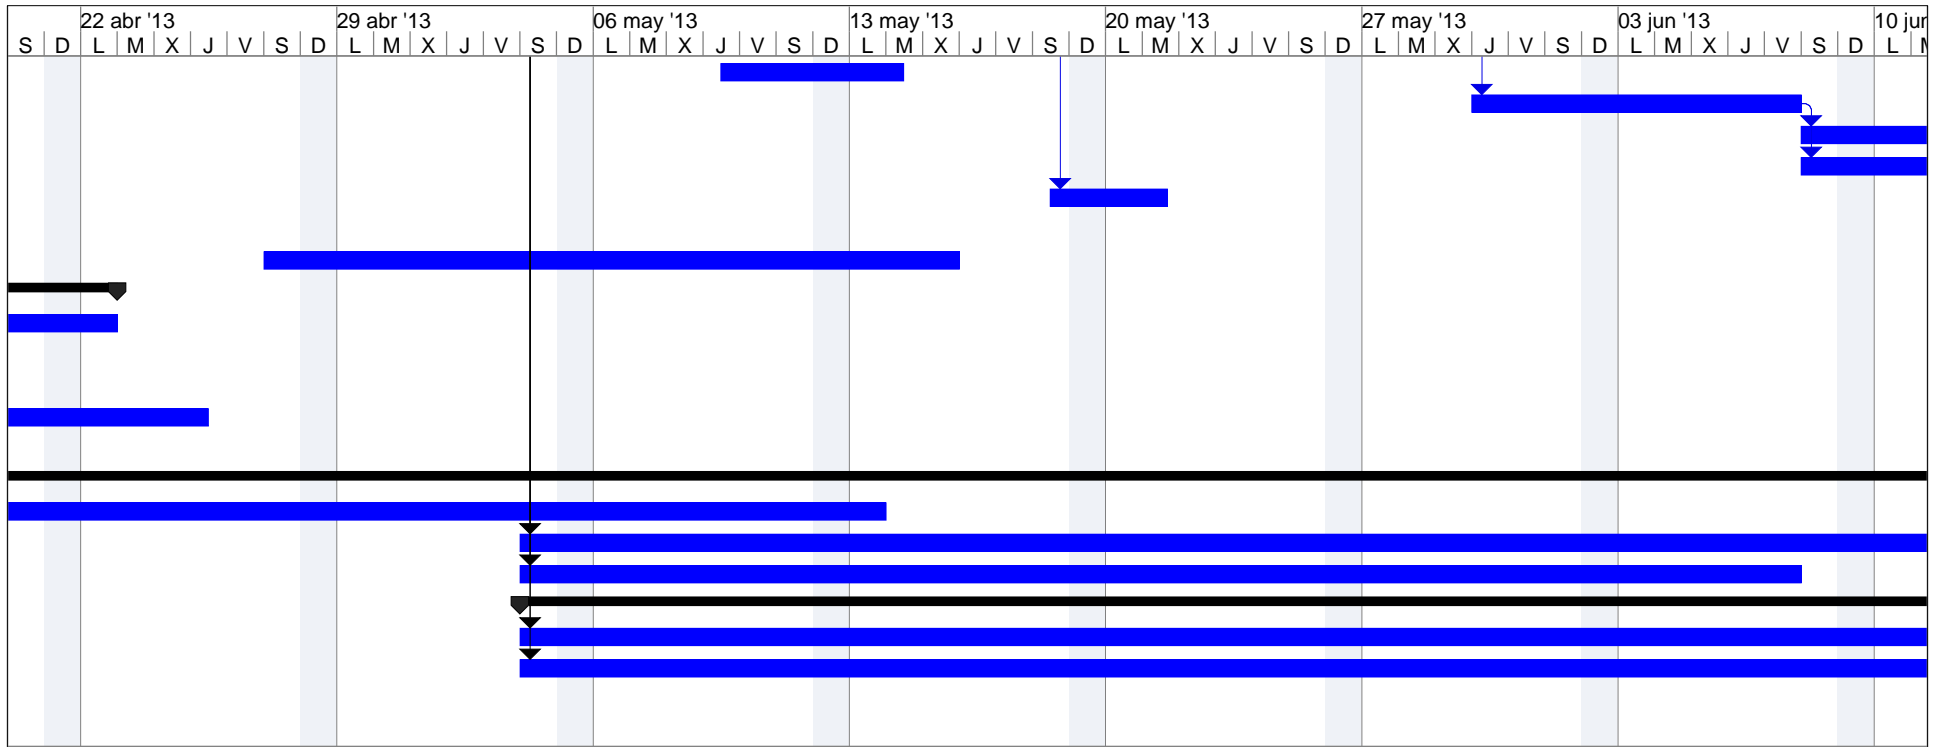

Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

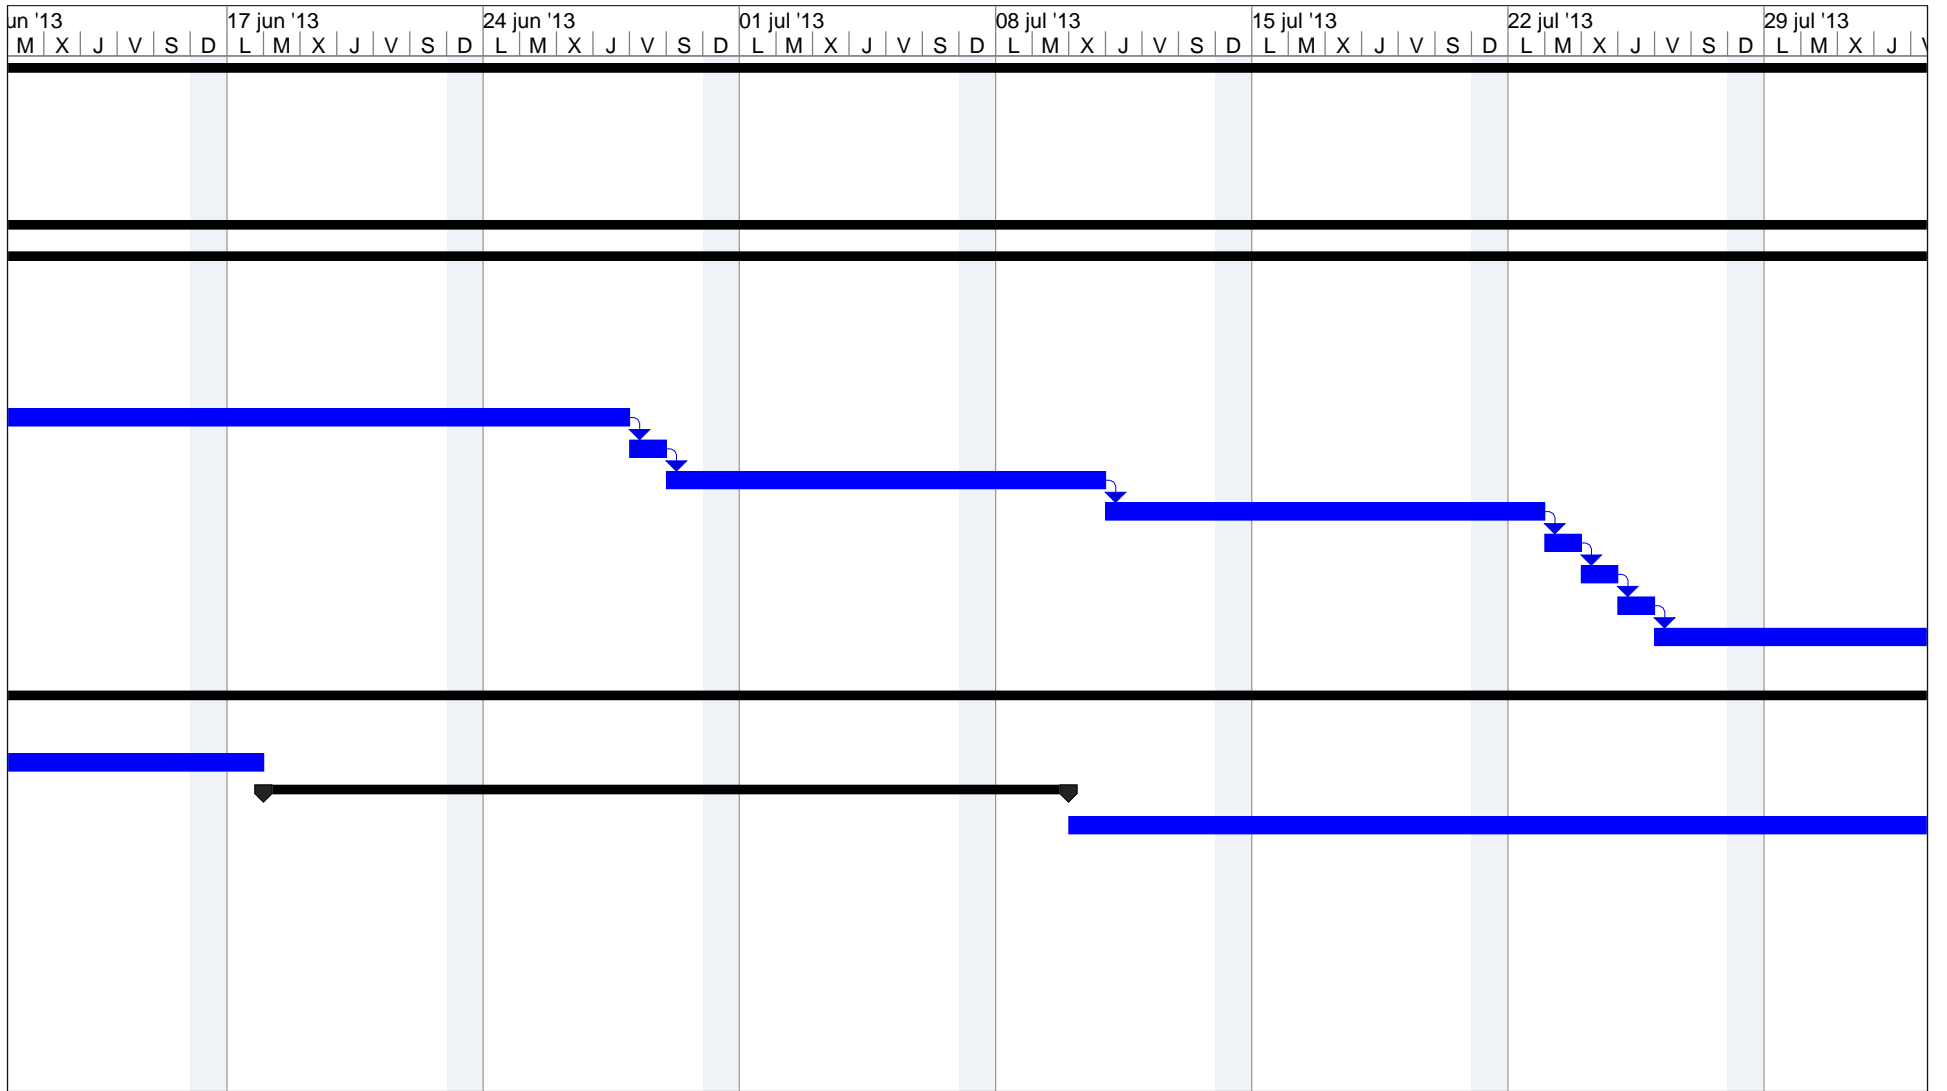


Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	




Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

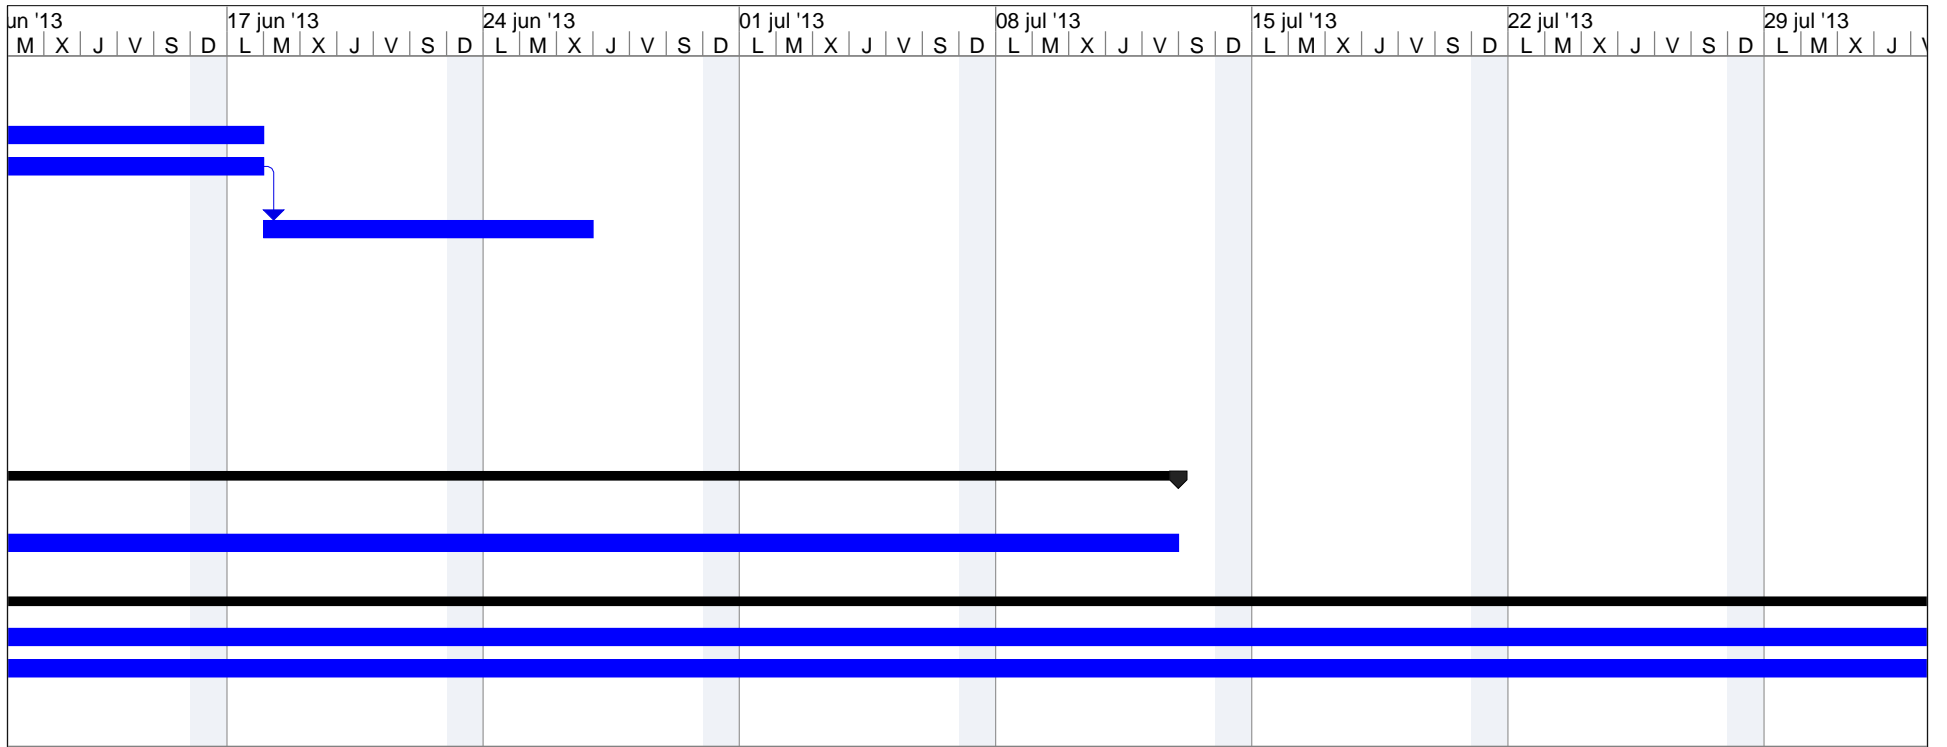

Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

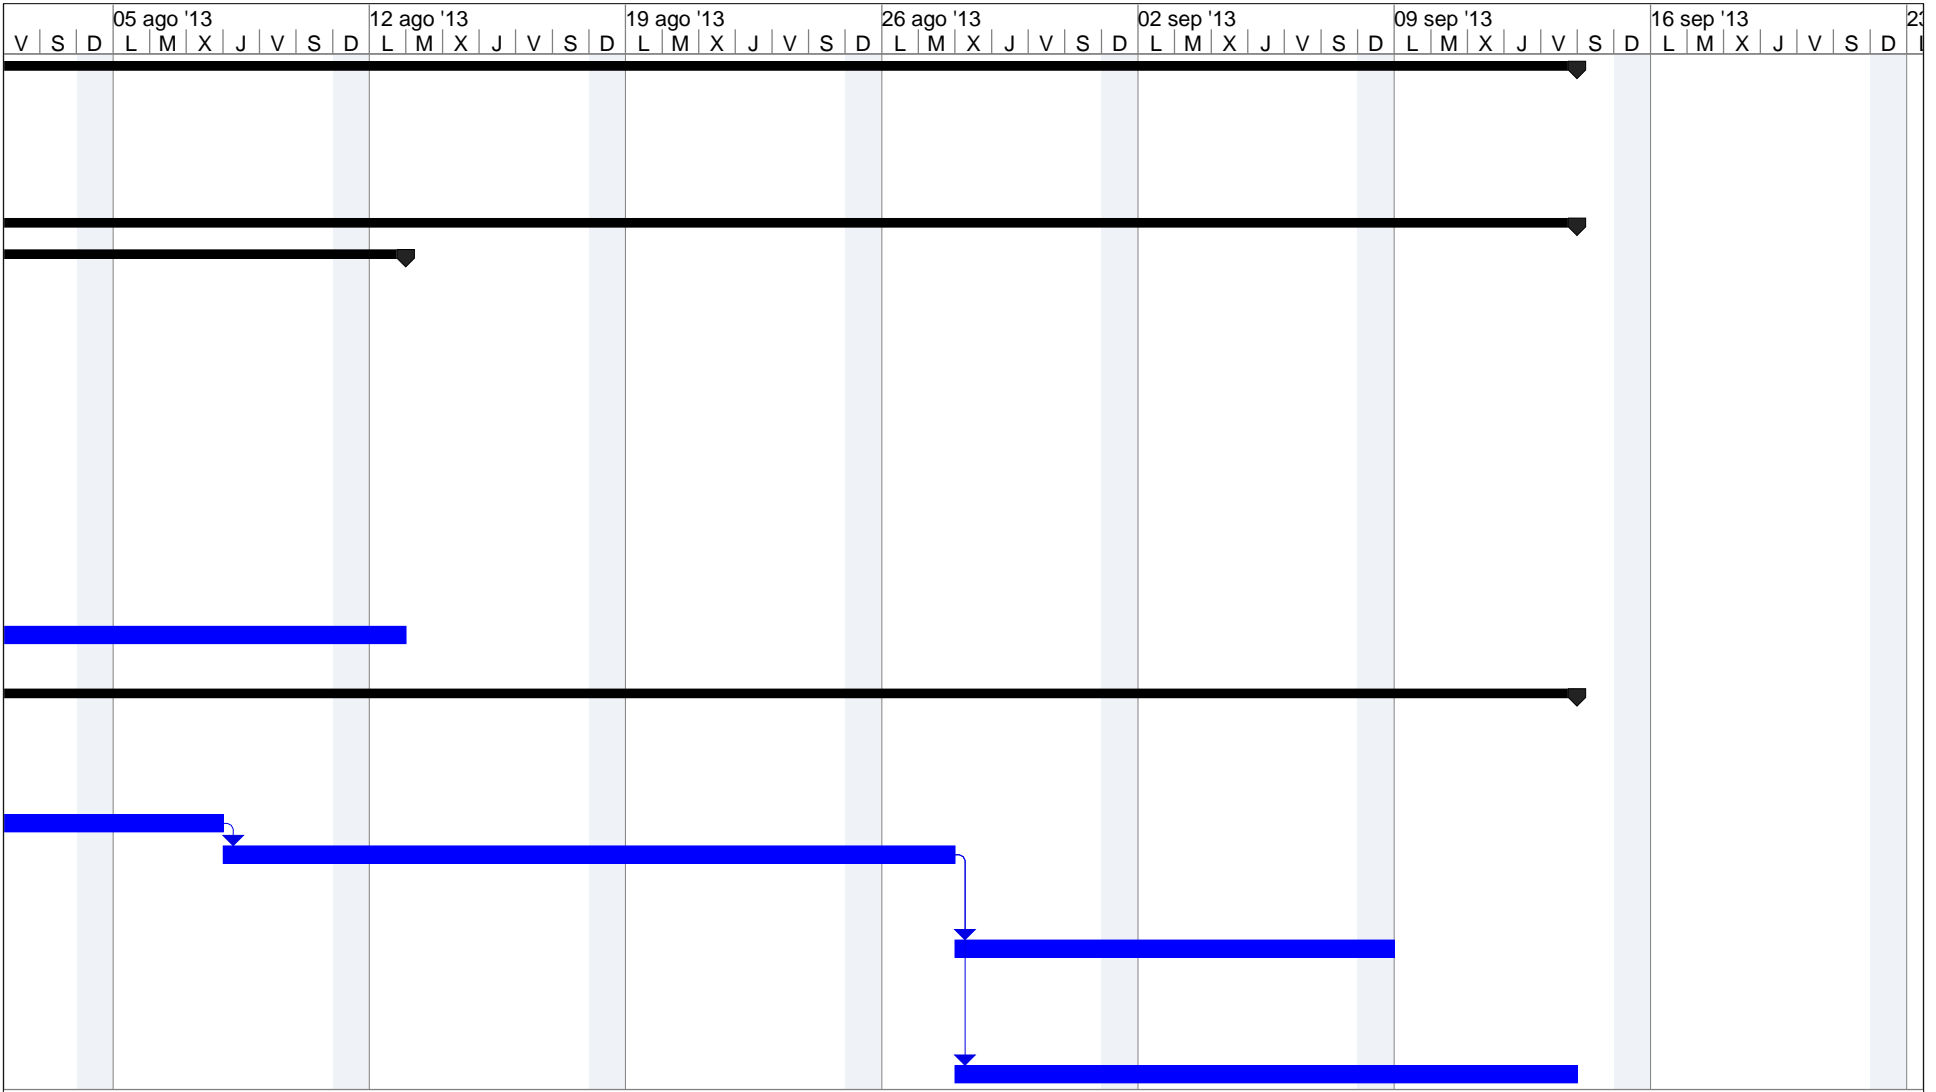


Project: LICEO ANA MARIA ALCANTA
 Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	



Project: LICEO ANA MARIA ALCANTARA
 Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

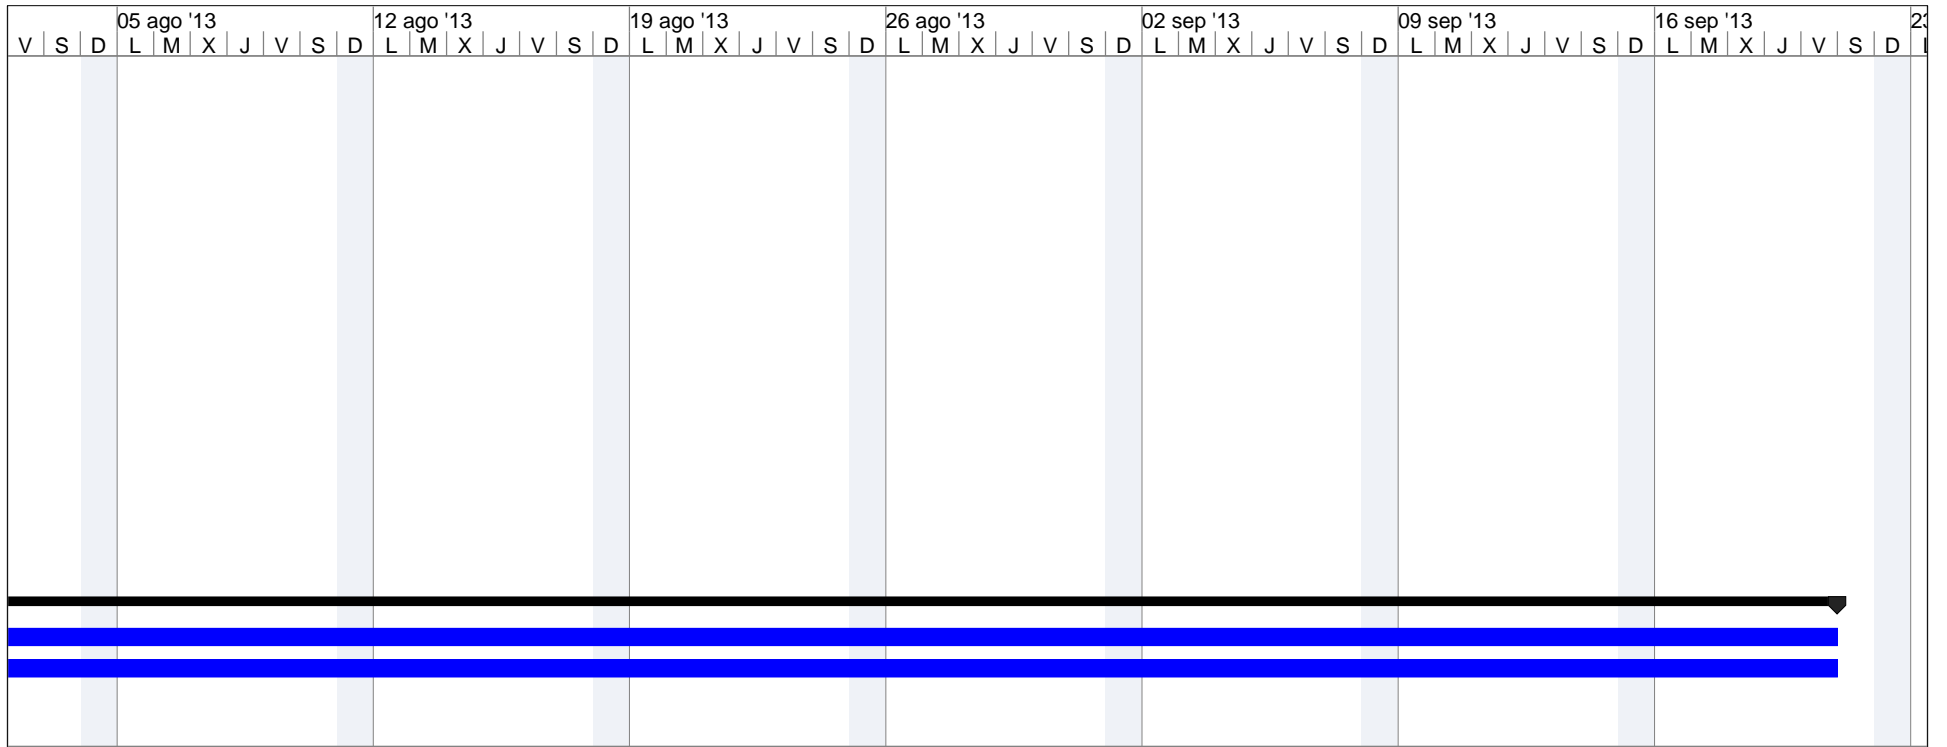

Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	
