


Id	Task Name	Duración	Comienzo	Fin	01 abr '13							08 abr '13							15 abr '13						
					S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V
1	BASICA BARRIO LA CARRETERA	144 días?	sáb 30/03/13	sáb 14/09/13																					
2	Preliminares	5 días	sáb 30/03/13	vie 05/04/13																					
3	Letrero en Obra	1 día	sáb 30/03/13	lun 01/04/13																					
4	Caseta de Materiales	2 días	lun 01/04/13	mié 03/04/13																					
5	Acondicionamiento de Terreno	4 días	lun 01/04/13	vie 05/04/13																					
6	BLOQUE B1	144 días?	sáb 30/03/13	sáb 14/09/13																					
7	B-1 >> 1er. NIVEL	116 días?	sáb 30/03/13	mar 13/08/13																					
8	Replanteo	2 días	vie 05/04/13	lun 08/04/13																					
9	Movimientos de Tierra	23 días	lun 08/04/13	sáb 04/05/13																					
12	Muros de Bloques	24 días	sáb 20/04/13	sáb 18/05/13																					
15	Hormigones	41 días	mié 17/04/13	mar 04/06/13																					
21	Terminacion de Superficies	21 días	mar 04/06/13	vie 28/06/13																					
22	Terminacion de Escalera	1 día?	vie 28/06/13	sáb 29/06/13																					
23	Terminacion de Piso	10 días	sáb 29/06/13	jue 11/07/13																					
24	Portaje Ventana y Protectores	10 días	jue 11/07/13	mar 23/07/13																					
25	Revestimiento de baño	1 día?	mar 23/07/13	mié 24/07/13																					
26	Plafones	1 día?	mié 24/07/13	jue 25/07/13																					
27	Aceras perimetrales	1 día?	jue 25/07/13	vie 26/07/13																					
28	Pintura	15 días	vie 26/07/13	mar 13/08/13																					
29	Varios	1 día?	sáb 30/03/13	lun 01/04/13																					
30	B-1>> 2do. NIVEL	144 días?	sáb 30/03/13	sáb 14/09/13																					
31	Replanteo	2 días	mar 04/06/13	jue 06/06/13																					
32	Muros de Bloques	10 días	jue 06/06/13	mar 18/06/13																					
33	Hormigones	19 días	mar 18/06/13	mié 10/07/13																					
36	Terminacion de Superficies	25 días	mié 10/07/13	jue 08/08/13																					
37	Terminacion de Piso	17 días	jue 08/08/13	mié 28/08/13																					
38	Terminacion de Escalera	7 días	sáb 30/03/13	lun 08/04/13																					
39	Portaje y Ventanas	10 días	mié 28/08/13	lun 09/09/13																					
40	Barandas	1 día?	sáb 30/03/13	lun 01/04/13																					
41	Revestimiento de baño	1 día?	sáb 30/03/13	lun 01/04/13																					
42	Plafones	1 día?	sáb 30/03/13	lun 01/04/13																					
43	Pintura	15 días	mié 28/08/13	sáb 14/09/13																					
44	Varios	12 días	mié 10/07/13	mié 24/07/13																					

Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

Id	Task Name	Duración	Comienzo	Fin	01 abr '13							08 abr '13							15 abr '13						
					S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V
45	B-1>>> 3er. NIVEL	1 día?	sáb 30/03/13	lun 01/04/13																					
46	Replanteo	1 día?	sáb 30/03/13	lun 01/04/13																					
47	Muros de Bloques	1 día?	sáb 30/03/13	lun 01/04/13																					
48	Hormigones	1 día?	sáb 30/03/13	lun 01/04/13																					
53	Terminacion de Superficies	1 día?	sáb 30/03/13	lun 01/04/13																					
54	Terminicacion de Piso	1 día?	sáb 30/03/13	lun 01/04/13																					
55	Terminacion de Escalera	1 día?	sáb 30/03/13	lun 01/04/13																					
56	Terminacion de techo	1 día?	sáb 30/03/13	lun 01/04/13																					
57	Revestimiento de baño	1 día?	sáb 30/03/13	lun 01/04/13																					
58	Portaje , Ventanas y Barandas	1 día?	sáb 30/03/13	lun 01/04/13																					
59	Pintura	1 día?	sáb 30/03/13	lun 01/04/13																					
60	Plafones	1 día?	sáb 30/03/13	lun 01/04/13																					
61	Varios	1 día?	sáb 30/03/13	lun 01/04/13																					
62	B-1>>> 4to. N. = Caja de Escalera <<	1 día?	sáb 30/03/13	lun 01/04/13																					
63	Replanteo	1 día?	sáb 30/03/13	lun 01/04/13																					
64	Hormigones	1 día?	sáb 30/03/13	lun 01/04/13																					
69	Muros de Bloques	1 día?	sáb 30/03/13	lun 01/04/13																					
70	Terminacion de Superficies	1 día?	sáb 30/03/13	lun 01/04/13																					
71	Terminacion de techo	1 día?	sáb 30/03/13	lun 01/04/13																					
72	Portaje y Ventanas	1 día?	sáb 30/03/13	lun 01/04/13																					
73	Pintura	1 día?	sáb 30/03/13	lun 01/04/13																					
74	Varios	1 día?	sáb 30/03/13	lun 01/04/13																					
75	BLOQUE B2	150 días?	sáb 30/03/13	sáb 21/09/13																					
76	B-2-1ER NIVEL	1 día?	sáb 30/03/13	lun 01/04/13																					
77	Replanteo	1 día?	sáb 30/03/13	lun 01/04/13																					
78	Muros de Bloques	1 día?	sáb 30/03/13	lun 01/04/13																					
79	Hormigones	1 día?	sáb 30/03/13	lun 01/04/13																					
82	Terminacion de Superficies	1 día?	sáb 30/03/13	lun 01/04/13																					
83	Terminicacion de Piso	1 día?	sáb 30/03/13	lun 01/04/13																					
84	Terminacion de Escalera	1 día?	sáb 30/03/13	lun 01/04/13																					
85	Aceras perimetrales	1 día?	sáb 30/03/13	lun 01/04/13																					
86	Portaje y Ventanas	1 día?	sáb 30/03/13	lun 01/04/13																					
87	Revestimiento de baño	1 día?	sáb 30/03/13	lun 01/04/13																					

Id	Task Name	Duración	Comienzo	Fin			01 abr '13							08 abr '13							15 abr '13																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
					S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
88	Protectores metalicos	1 día?	sáb 30/03/13	lun 01/04/13																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				</

Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	


Id	Task Name	Duración	Comienzo	Fin	01 abr '13							08 abr '13							15 abr '13						
					S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V
121	Terminacion de Superficies	1 día?	sáb 30/03/13	lun 01/04/13																					
122	Terminacion de techo	1 día?	sáb 30/03/13	lun 01/04/13																					
123	Portaje y Ventanas	1 día?	sáb 30/03/13	lun 01/04/13																					
124	Pintura	1 día?	sáb 30/03/13	lun 01/04/13																					
125	Varios	1 día?	sáb 30/03/13	lun 01/04/13																					
126	BLOQUE B3	1 día?	sáb 30/03/13	lun 01/04/13																					
127	B-3-1ER NIVEL	1 día?	sáb 30/03/13	lun 01/04/13																					
128	Replanteo	1 día?	sáb 30/03/13	lun 01/04/13																					
129	Muros de Bloques	1 día?	sáb 30/03/13	lun 01/04/13																					
130	Hormigones	1 día?	sáb 30/03/13	lun 01/04/13																					
131	Terminacion de Superficies	1 día?	sáb 30/03/13	lun 01/04/13																					
132	Terminacion de Piso	1 día?	sáb 30/03/13	lun 01/04/13																					
133	Terminacion de techo	1 día?	sáb 30/03/13	lun 01/04/13																					
134	Aceras perimetrales	1 día?	sáb 30/03/13	lun 01/04/13																					
135	Portaje y Ventanas	1 día?	sáb 30/03/13	lun 01/04/13																					
136	Revestimiento de baño	1 día?	sáb 30/03/13	lun 01/04/13																					
137	Protectores metalicos	1 día?	sáb 30/03/13	lun 01/04/13																					
138	Plafones	1 día?	sáb 30/03/13	lun 01/04/13																					
139	Pintura	1 día?	sáb 30/03/13	lun 01/04/13																					
140	Varios	1 día?	sáb 30/03/13	lun 01/04/13																					
141	BLOQUE B4 (3 Aula Inicial + Baños)	1 día?	sáb 30/03/13	lun 01/04/13																					
142	Replanteo	1 día?	sáb 30/03/13	lun 01/04/13																					
143	Muros de Bloques	1 día?	sáb 30/03/13	lun 01/04/13																					
144	Hormigones	1 día?	sáb 30/03/13	lun 01/04/13																					
145	Terminacion de Superficies	1 día?	sáb 30/03/13	lun 01/04/13																					
146	Terminacion de Piso	1 día?	sáb 30/03/13	lun 01/04/13																					
147	Terminacion de techo	1 día?	sáb 30/03/13	lun 01/04/13																					
148	Aceras perimetrales	1 día?	sáb 30/03/13	lun 01/04/13																					
149	Portaje y Ventanas	1 día?	sáb 30/03/13	lun 01/04/13																					
150	Revestimiento de baño	1 día?	sáb 30/03/13	lun 01/04/13																					
151	Protectores metalicos	1 día?	sáb 30/03/13	lun 01/04/13																					
152	Plafones	1 día?	sáb 30/03/13	lun 01/04/13																					
153	Pintura	1 día?	sáb 30/03/13	lun 01/04/13																					


Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

Id	Task Name	Duración	Comienzo	Fin	01 abr '13							08 abr '13							15 abr '13						
					S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V
154	Areas recreo educ. inicial+otros	1 día?	sáb 30/03/13	lun 01/04/13																					
155	COMEDOR 256 PERSONAS	76 días?	sáb 30/03/13	jue 27/06/13																					
156	Replanteo	0.8 días	sáb 30/03/13	sáb 30/03/13																					
157	Muros de Bloques	16 días	sáb 30/03/13	jue 18/04/13																					
158	Hormigones	1 día?	sáb 30/03/13	lun 01/04/13																					
159	Terminacion de Superficies	18.4 días	jue 18/04/13	jue 09/05/13																					
164	Terminacion de Piso	8 días	jue 09/05/13	sáb 18/05/13																					
165	Terminacion de techo	9.6 días	sáb 18/05/13	jue 30/05/13																					
166	Revestimiento de baño	4 días	jue 09/05/13	mar 14/05/13																					
167	Portaje y Ventanas	8 días	jue 30/05/13	sáb 08/06/13																					
168	Protectores metalicos	8 días	sáb 08/06/13	mar 18/06/13																					
169	Pintura	8 días	sáb 08/06/13	mar 18/06/13																					
170	Aceras perimetrales	2.4 días	sáb 18/05/13	mar 21/05/13																					
171	Pintura	8 días	mar 18/06/13	jue 27/06/13																					
172	Varios	16 días	sáb 27/04/13	jue 16/05/13																					
173	OBRAS COMPLEMENTARIAS	20 días	sáb 30/03/13	mar 23/04/13																					
174	CISTERNA	20 días	sáb 30/03/13	mar 23/04/13																					
175	CAMARA SEPTICA DE DOS CAMARAS	12 días	sáb 30/03/13	sáb 13/04/13																					
176	CAMARA SEPTICA DE DOS CAMARAS	12 días	sáb 30/03/13	sáb 13/04/13																					
177	MISCELANEOS	5.6 días	sáb 30/03/13	vie 05/04/13																					
178	CANCHA MIXTA	22.4 días	sáb 30/03/13	jue 25/04/13																					
179	GRADERIA EN CANCHA	16 días	sáb 30/03/13	jue 18/04/13																					
180	Áreas Exteriores	90 días	sáb 30/03/13	sáb 13/07/13																					
181	Acondicionamiento del Area Exterior	38 días	sáb 30/03/13	mar 14/05/13																					
182	Verja Perimetral	60 días	sáb 04/05/13	sáb 13/07/13																					
183	Caseta de bomba y Cisterna	30 días	sáb 04/05/13	sáb 08/06/13																					
184	Instalaciones Eléctricas y Sanitarias	120 días	sáb 04/05/13	sáb 21/09/13																					
185	Instalacion Electrica General	120 días	sáb 04/05/13	sáb 21/09/13																					
186	Instalacion Sanitaria General	120 días	sáb 04/05/13	sáb 21/09/13																					
187	Adicionales	1 día?	sáb 30/03/13	lun 01/04/13																					
188	LIMPIEZA CONTINUA Y FINAL	1 día?	sáb 30/03/13	lun 01/04/13																					

Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18


Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

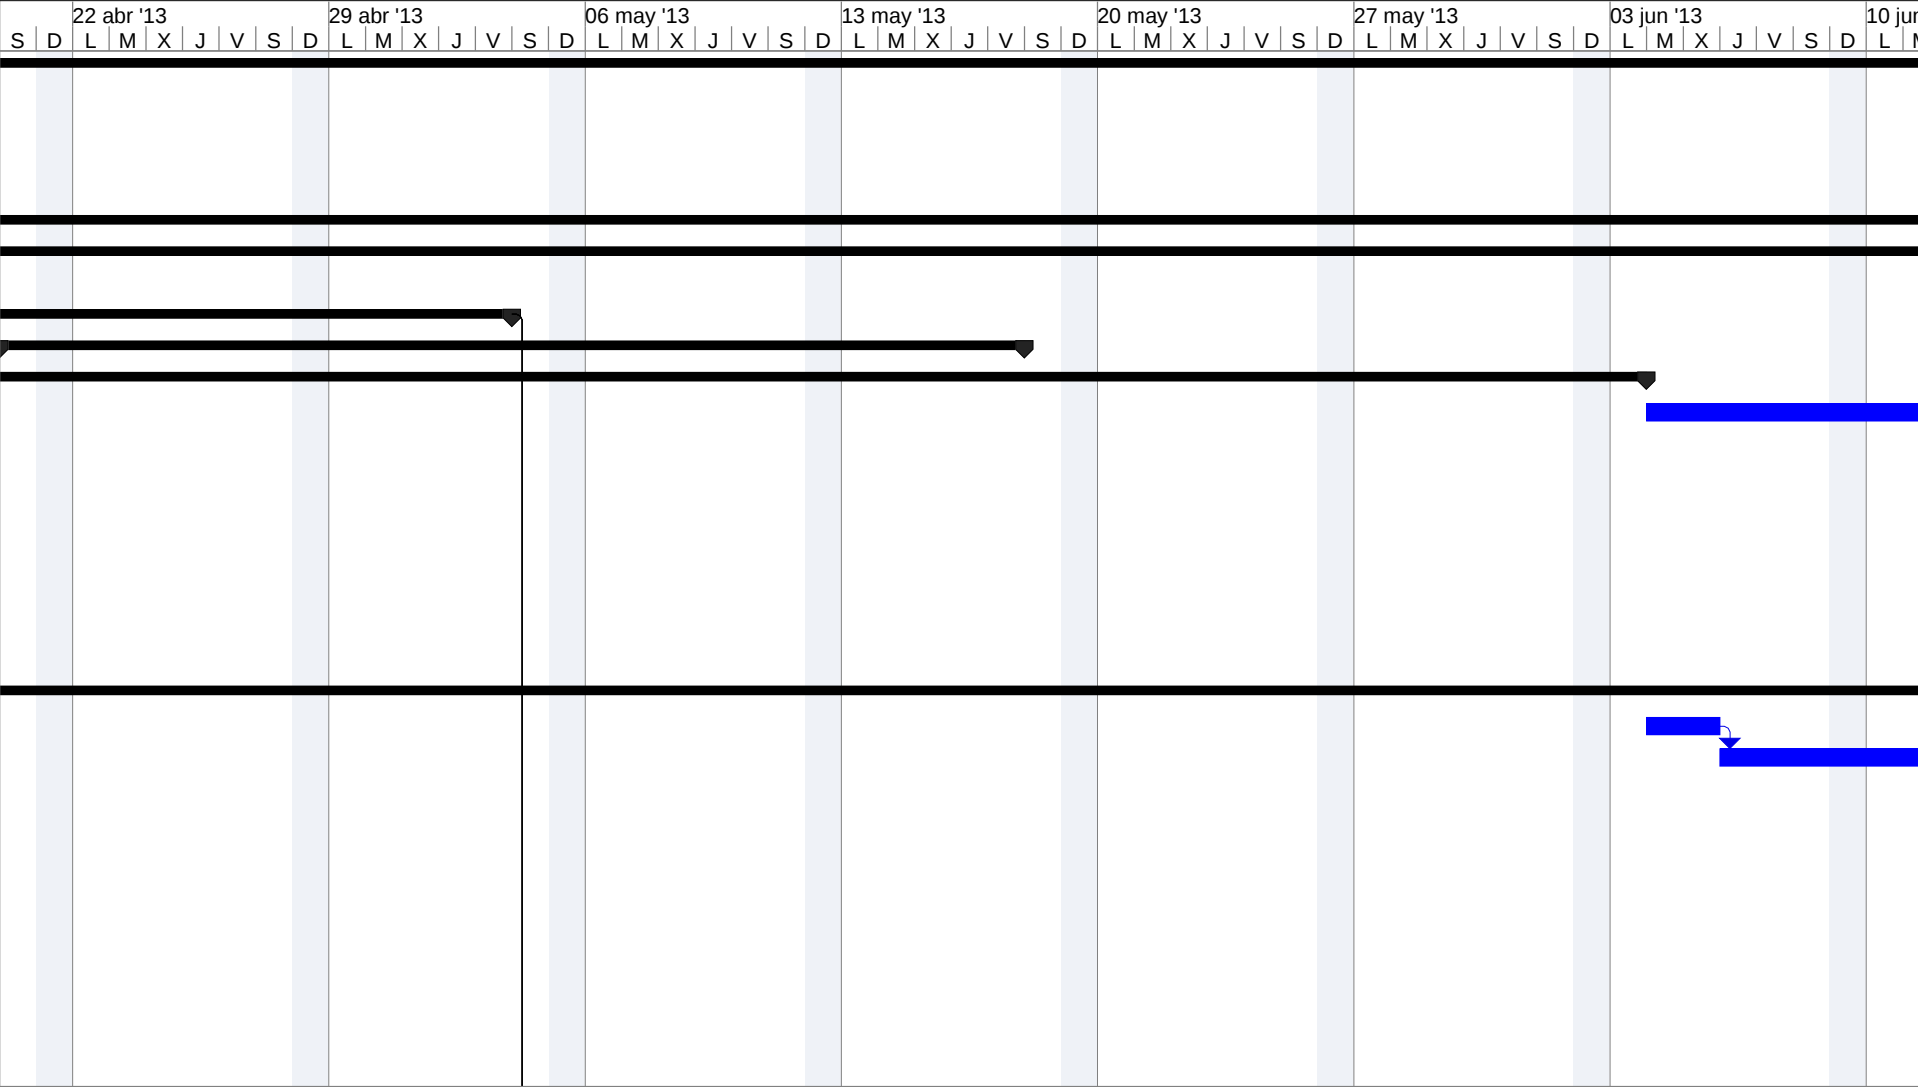

Project: LICEO ANA MARIA ALCANTA Date: vie 23/03/18	Task		External Tasks		Duration-only	
	Milestone		Project Summary		Manual Summary Rollup	
	Summary		Group By Summary		Manual Summary	
	Rolled Up Task		Inactive Task		Start-only	
	Rolled Up Milestone		Inactive Milestone		Finish-only	
	Rolled Up Progress		Inactive Summary		Progress	
	Split		Manual Task		Deadline	


[illegible][illegible]

Project: LICEO ANA MARIA ALCANTA Date: vie 23/03/18	Task		External Tasks		Duration-only	
	Milestone		Project Summary		Manual Summary Rollup	
	Summary		Group By Summary		Manual Summary	
	Rolled Up Task		Inactive Task		Start-only	
	Rolled Up Milestone		Inactive Milestone		Finish-only	
	Rolled Up Progress		Inactive Summary		Progress	
	Split		Manual Task		Deadline	

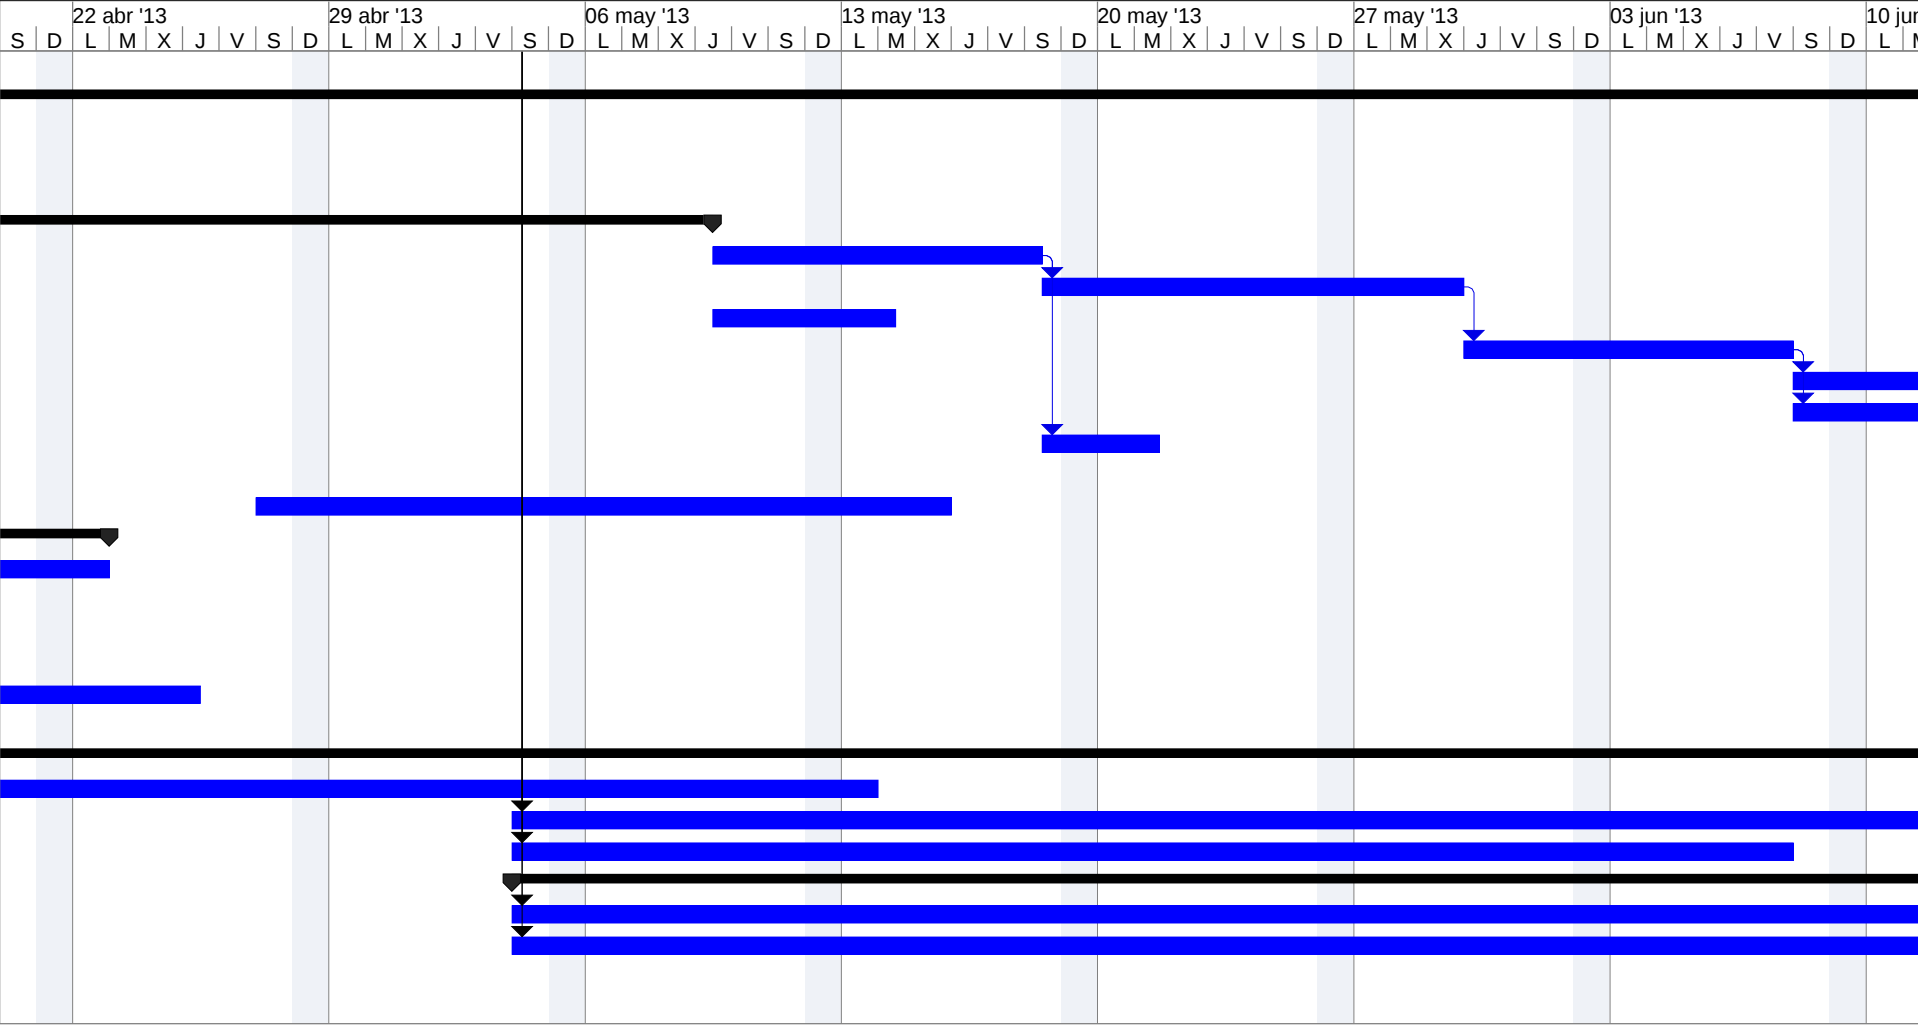


Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

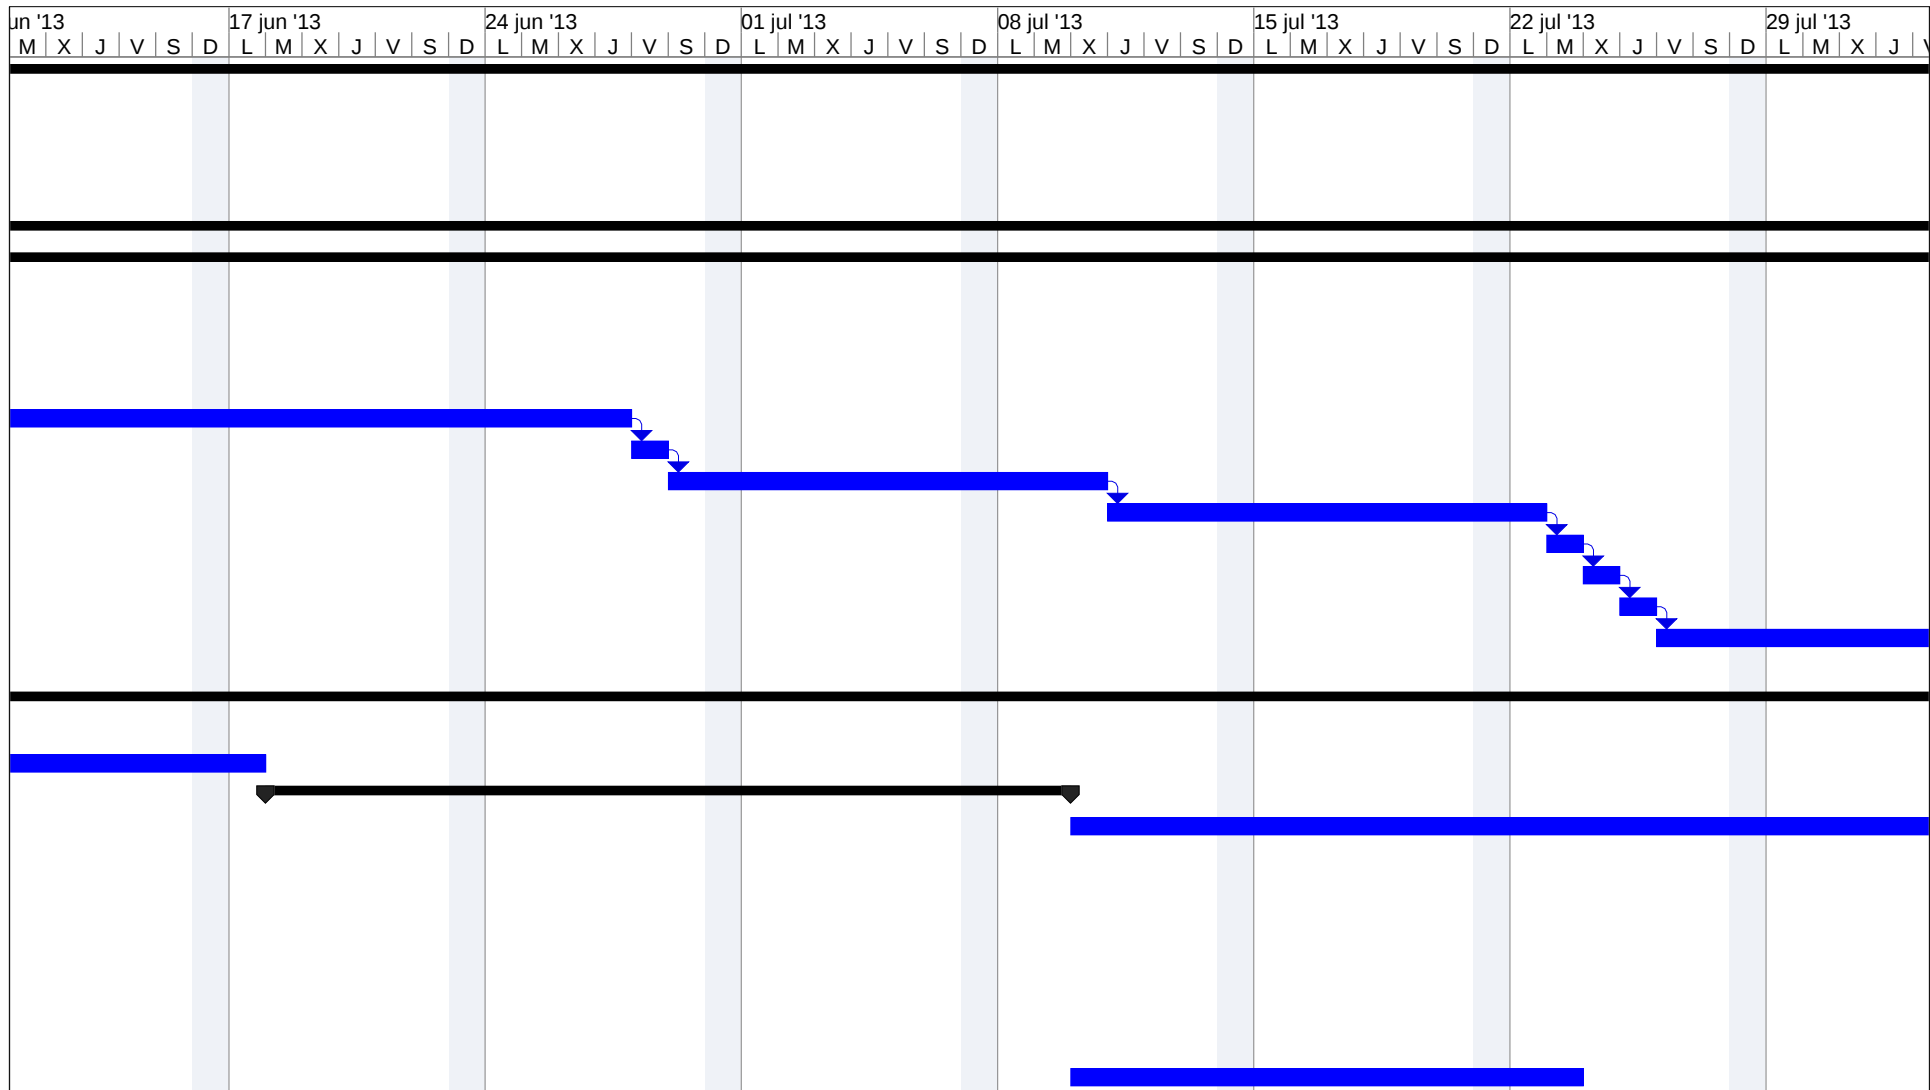

Project: LICEO ANA MARIA ALCANTARA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

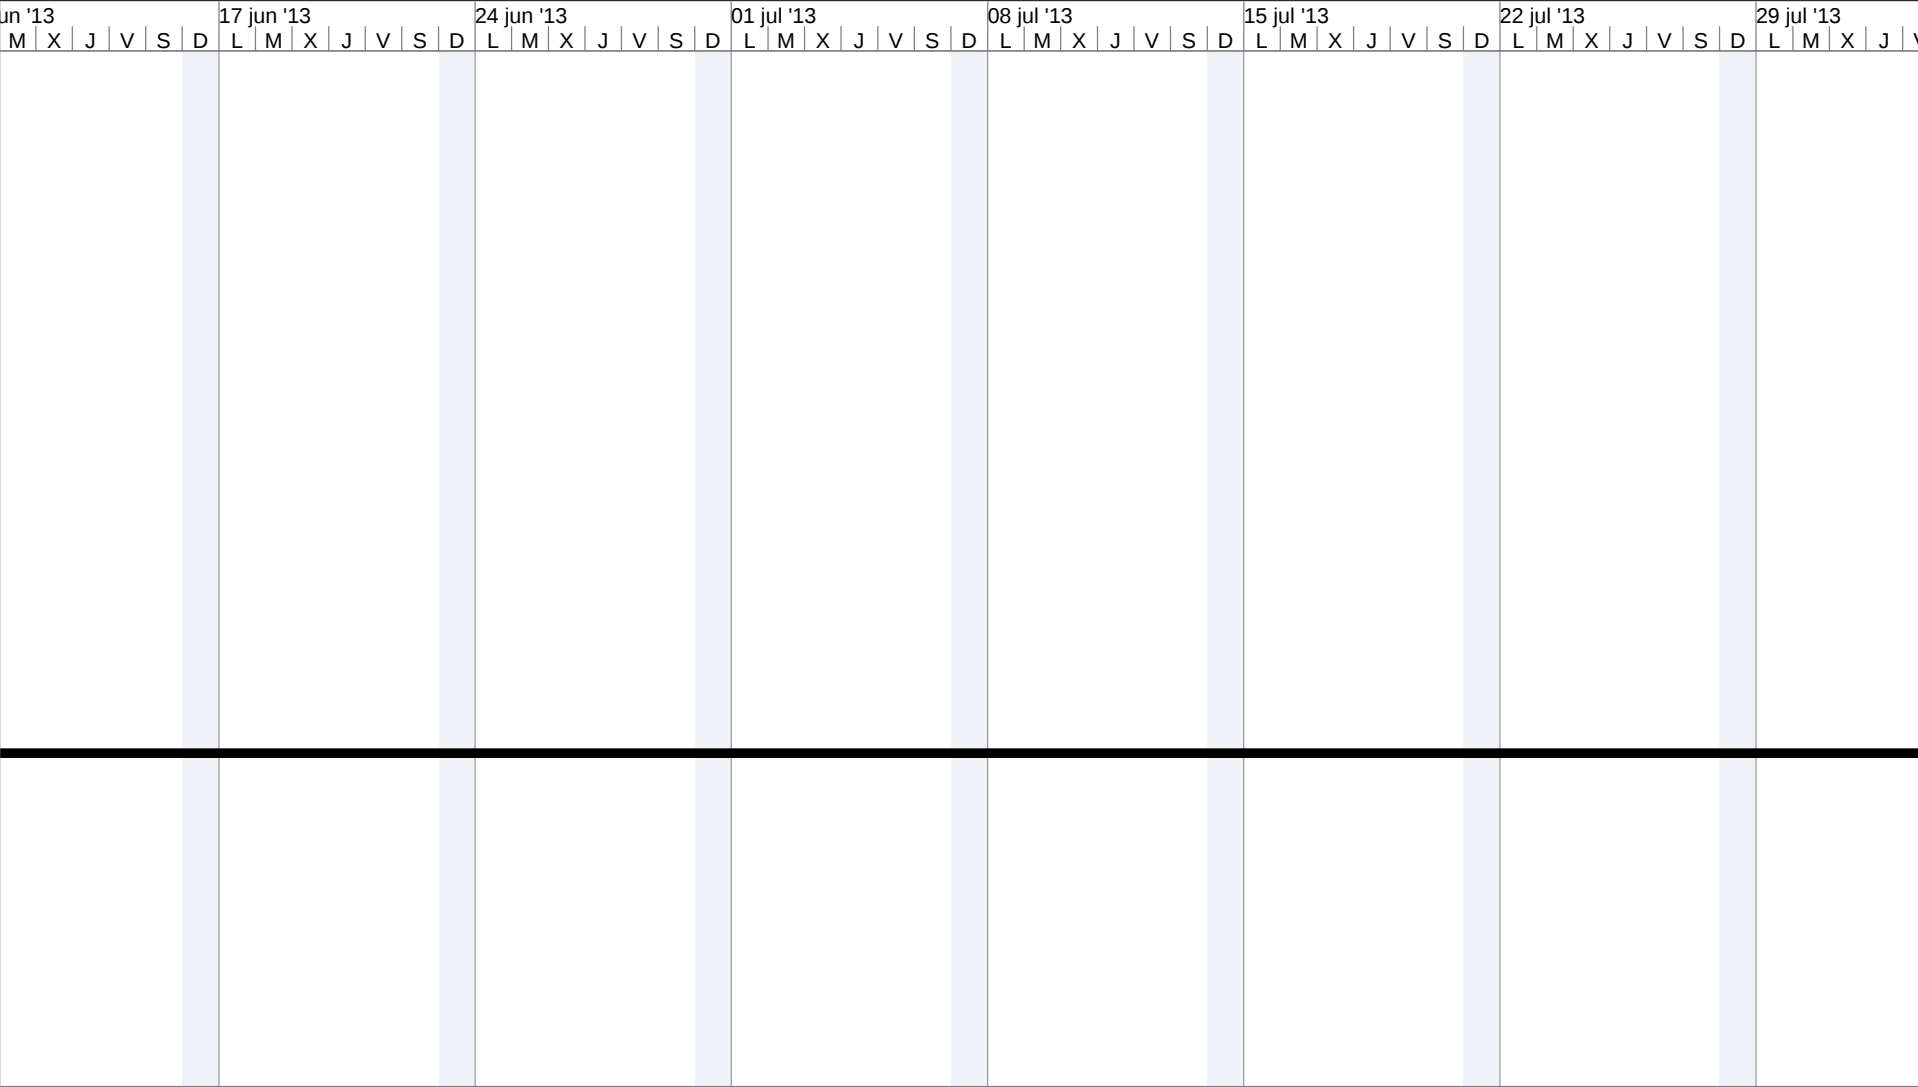

Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task

Milestone

Summary

Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

Split

External Tasks

Project Summary

Group By Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


Progress

Deadline



Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

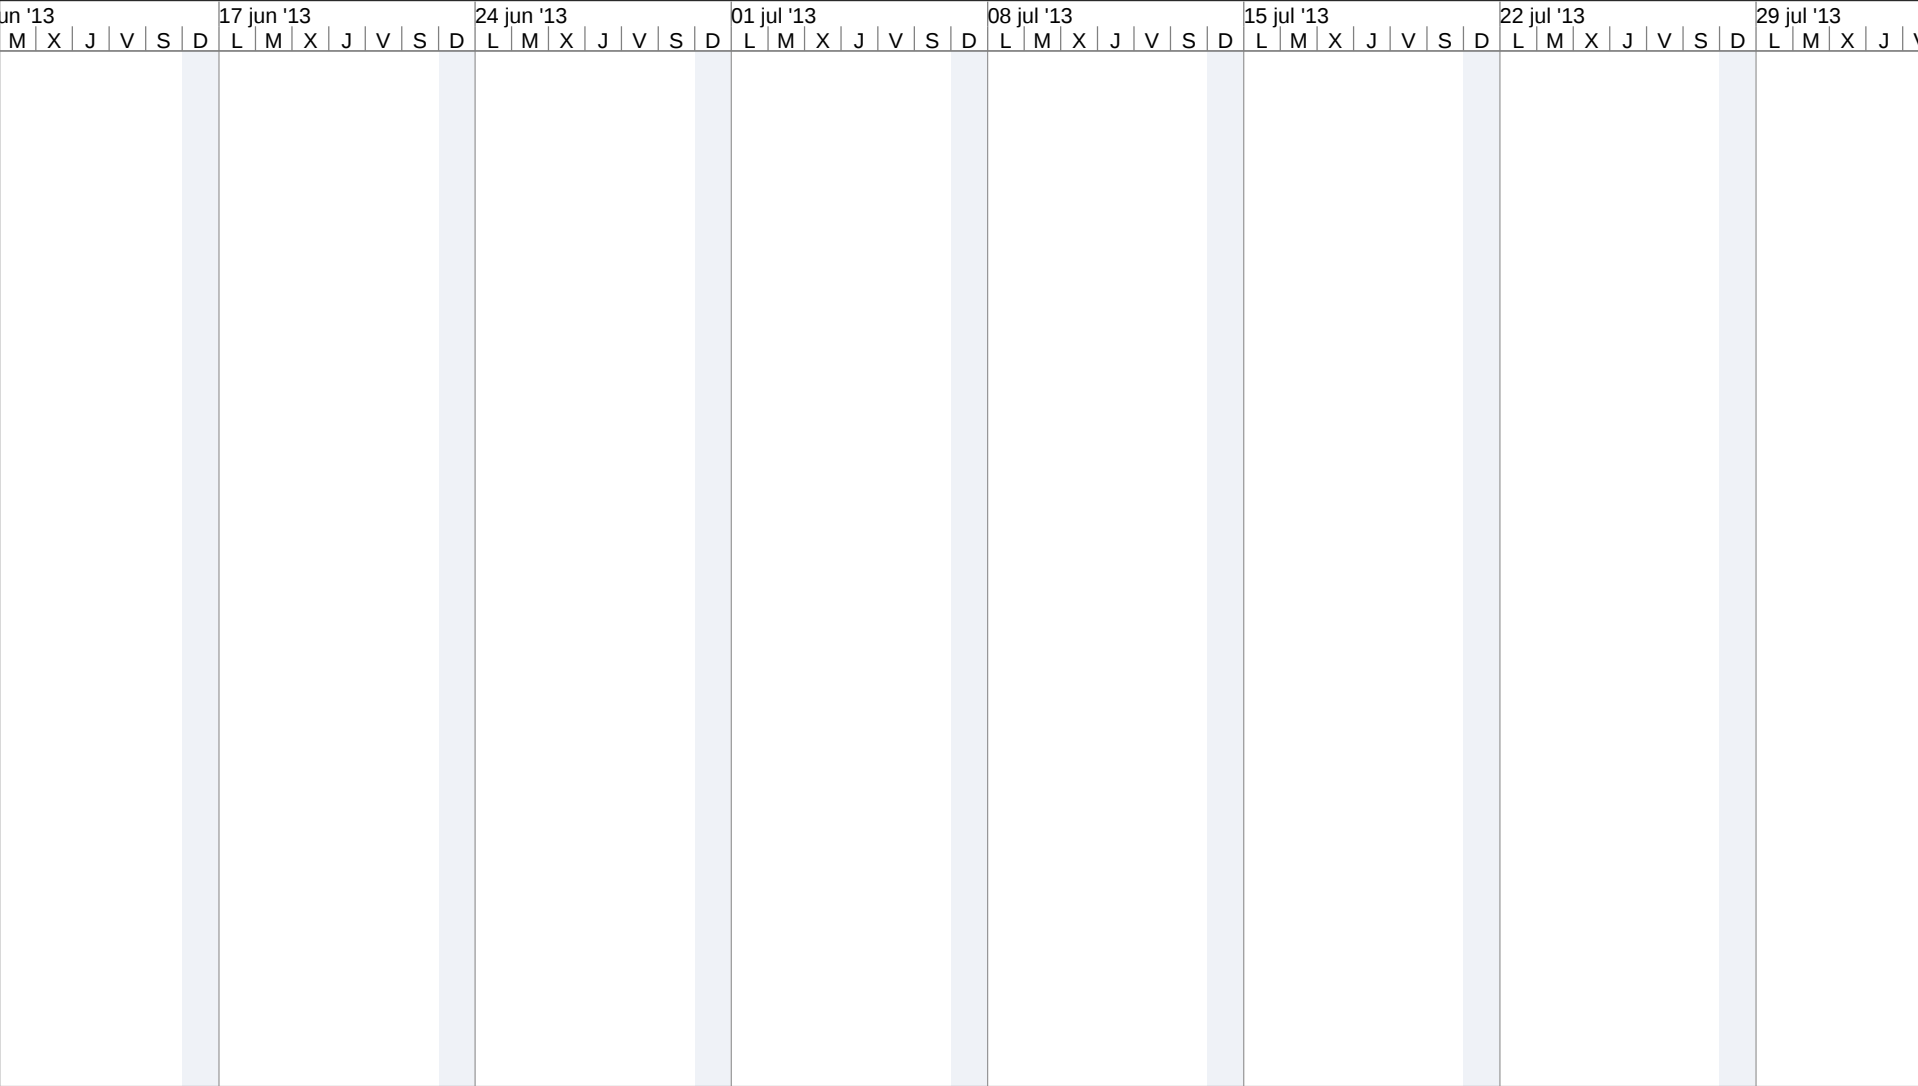


Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	



Project: LICEO ANA MARIA ALCANTA Date: vie 23/03/18	Task		External Tasks		Duration-only	
	Milestone		Project Summary		Manual Summary Rollup	
	Summary		Group By Summary		Manual Summary	
	Rolled Up Task		Inactive Task		Start-only	
	Rolled Up Milestone		Inactive Milestone		Finish-only	
	Rolled Up Progress		Inactive Summary		Progress	
	Split		Manual Task		Deadline	

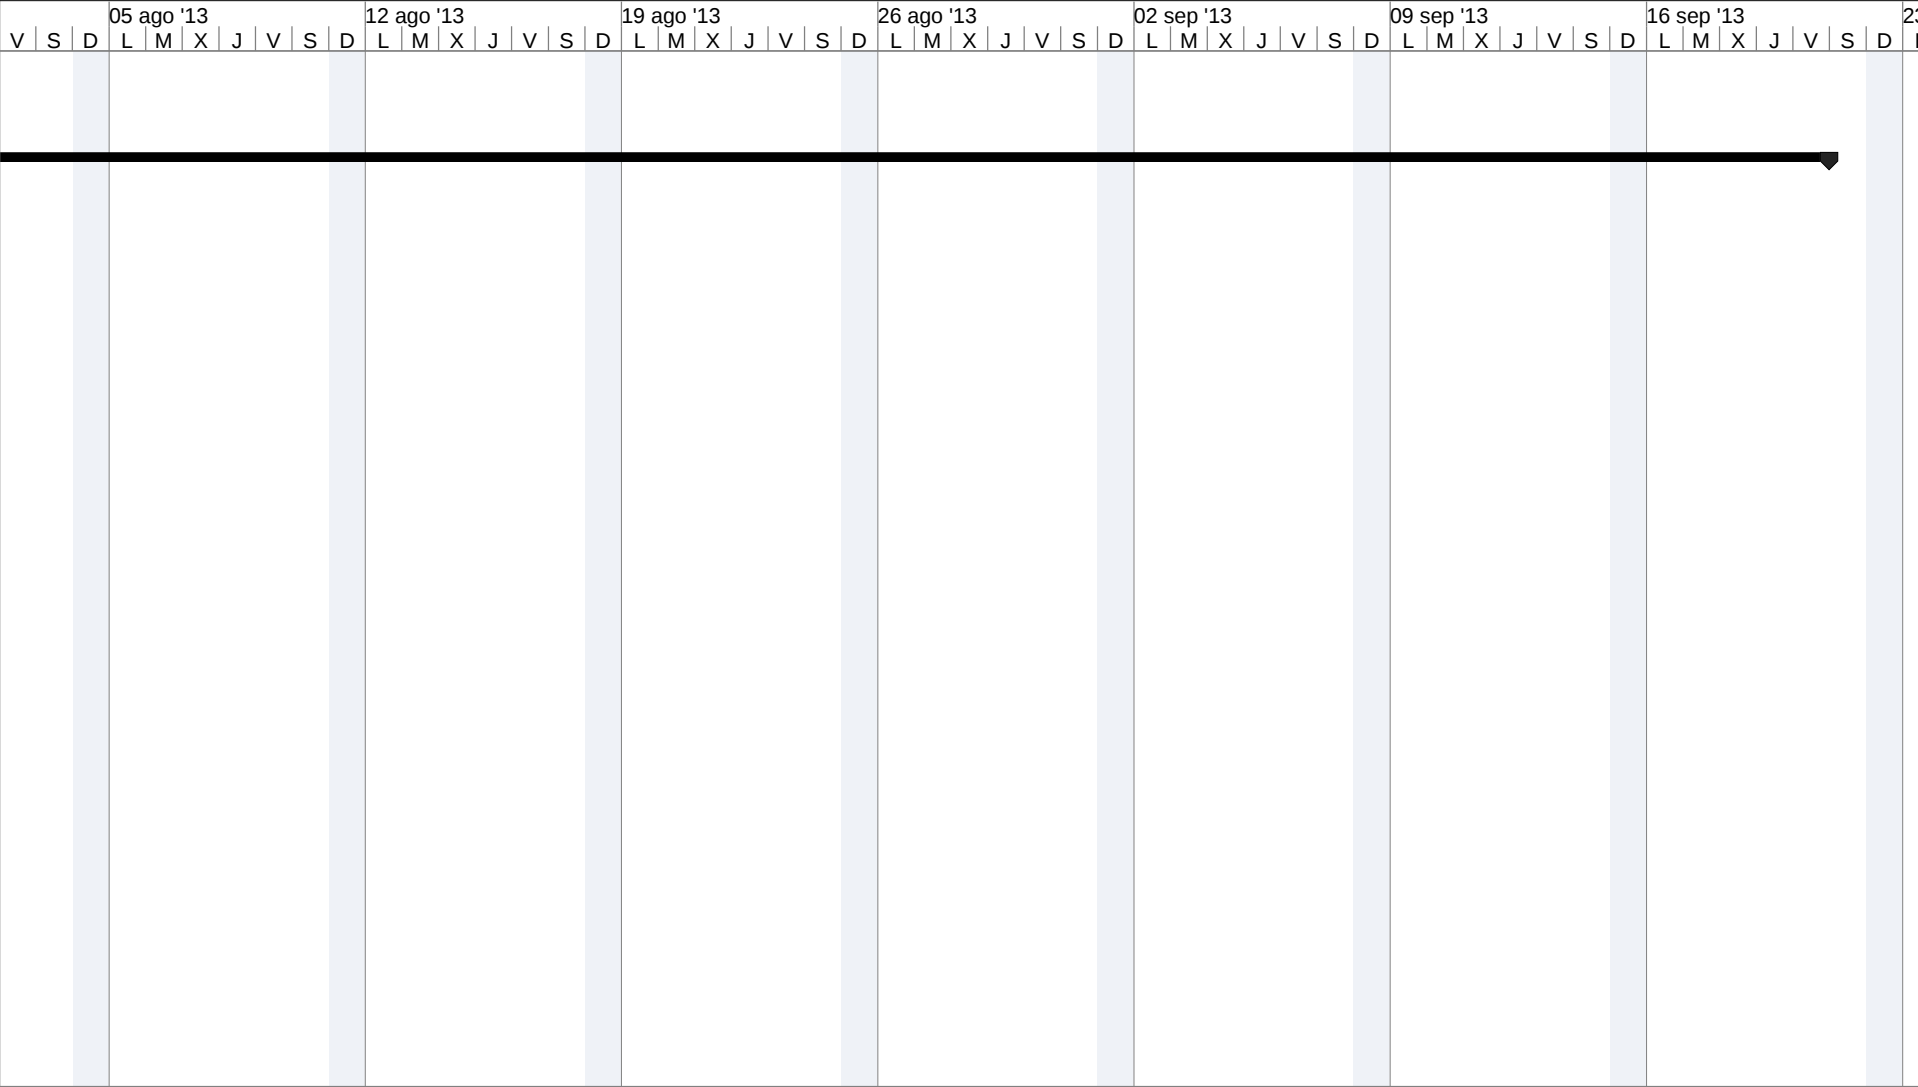


Project: LICEO ANA MARIA ALCANTA
Date: vie 23/03/18

Task		External Tasks		Duration-only	
Milestone		Project Summary		Manual Summary Rollup	
Summary		Group By Summary		Manual Summary	
Rolled Up Task		Inactive Task		Start-only	
Rolled Up Milestone		Inactive Milestone		Finish-only	
Rolled Up Progress		Inactive Summary		Progress	
Split		Manual Task		Deadline	

[illegible]

Project: LICEO ANA MARIA ALCANTA Date: vie 23/03/18	Task		External Tasks		Duration-only	
	Milestone		Project Summary		Manual Summary Rollup	
	Summary		Group By Summary		Manual Summary	
	Rolled Up Task		Inactive Task		Start-only	
	Rolled Up Milestone		Inactive Milestone		Finish-only	
	Rolled Up Progress		Inactive Summary		Progress	
	Split		Manual Task		Deadline	

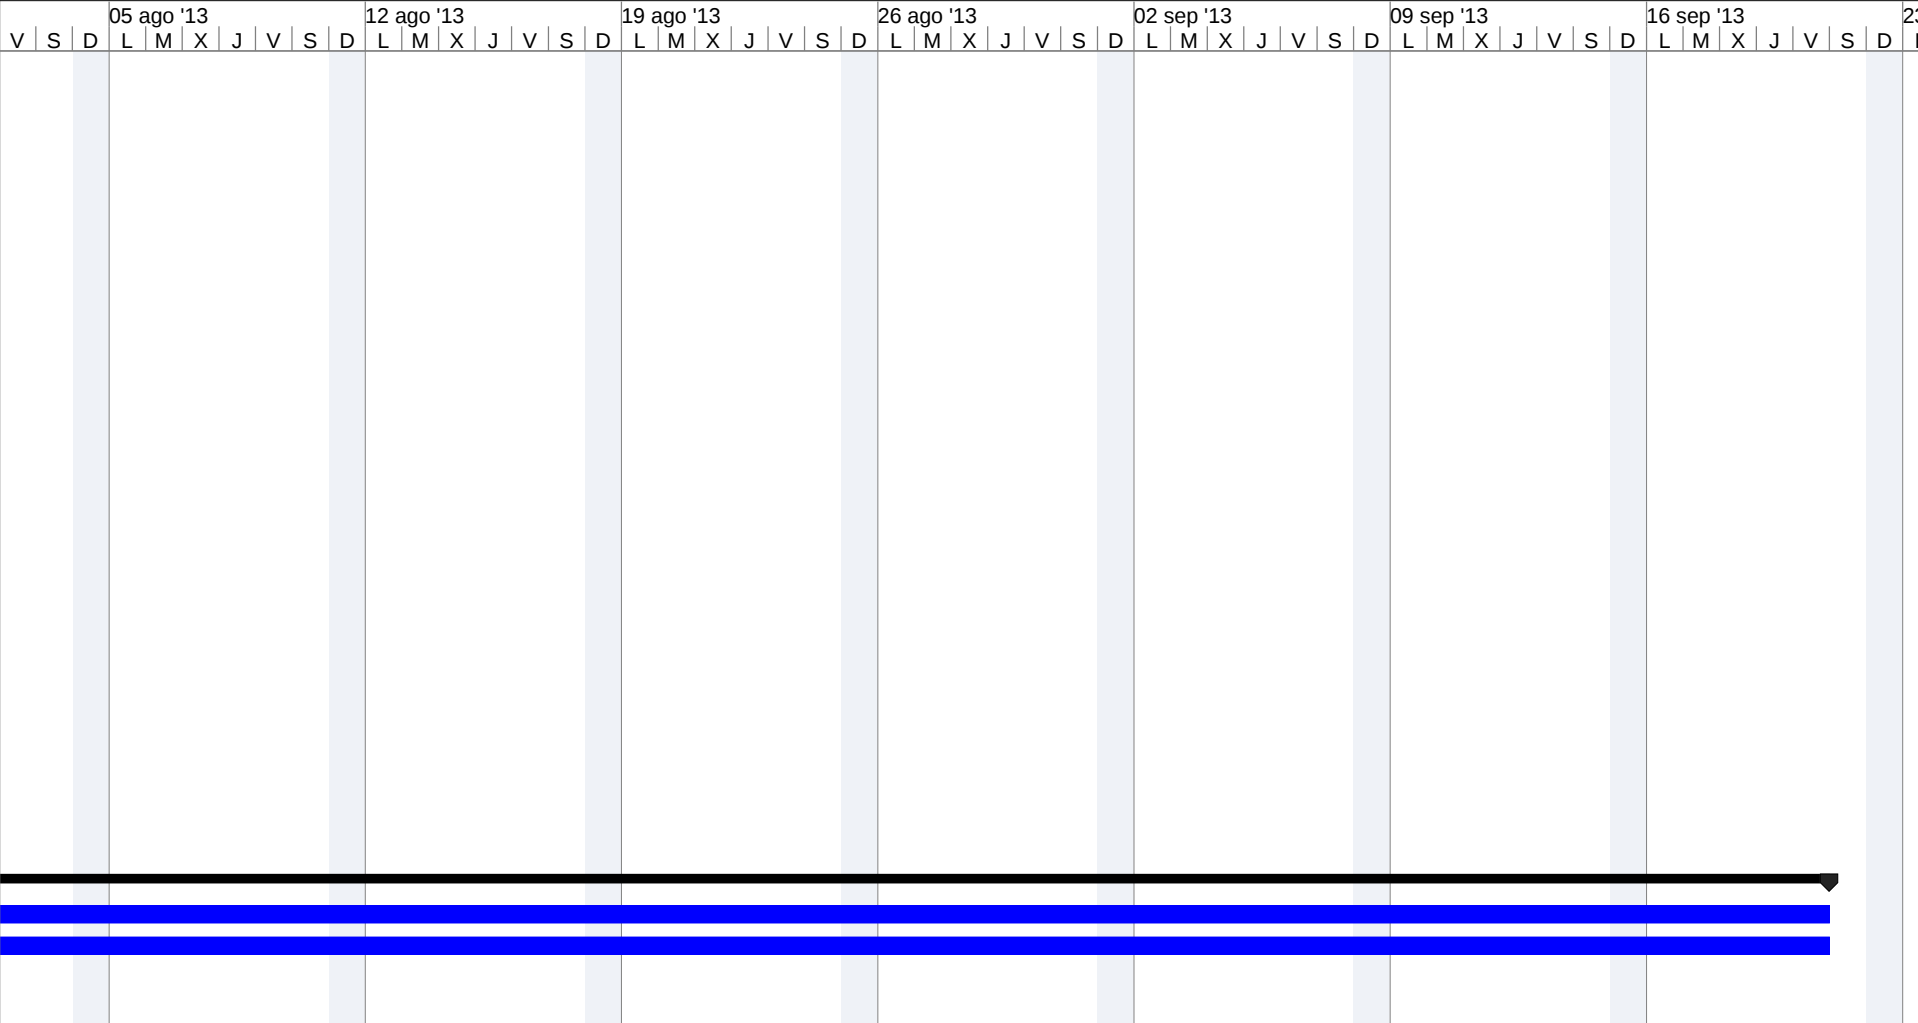

Project: LICEO ANA MARIA ALCANTA Date: vie 23/03/18	Task		External Tasks		Duration-only	
	Milestone		Project Summary		Manual Summary Rollup	
	Summary		Group By Summary		Manual Summary	
	Rolled Up Task		Inactive Task		Start-only	
	Rolled Up Milestone		Inactive Milestone		Finish-only	
	Rolled Up Progress		Inactive Summary		Progress	
	Split		Manual Task		Deadline	
